CONSULTANT: WEST / WVLA DESIGN -BUILD
CONTRACTOR: WEST CONSTRUCTION INC
FUNDS: 320

FLAMINGO PARK RENOVATION
PROJECT # 99615101

Project Manager: Jeff Halverson
Updated: Wed 1/16/08

ID	Task Name	Duration	Start	Finish
1	Community meetings and preliminary design.	102 days	Tue 3/21/06	Fri 6/30/06
2	**DESIGN**	**376 days**	**Tue 3/21/06**	**Sat 3/31/07**
3	SCHEMATIC DESIGN	114 days	Tue 3/21/06	Wed 7/12/06
4	FACE OF THE CITY PRESENTATION	1 day	Sun 8/27/06	Sun 8/27/06
5	FINAL DESIGN	216 days	Mon 8/28/06	Sat 3/31/07
6	**CONSTRUCTION**	**253 days**	**Sun 5/6/07**	**Sun 1/13/08**
7	PERMITTING	112 days	Sun 5/6/07	Sat 8/25/07
8	CONSTRUCT	120 days	Sun 9/16/07	Sun 1/13/08

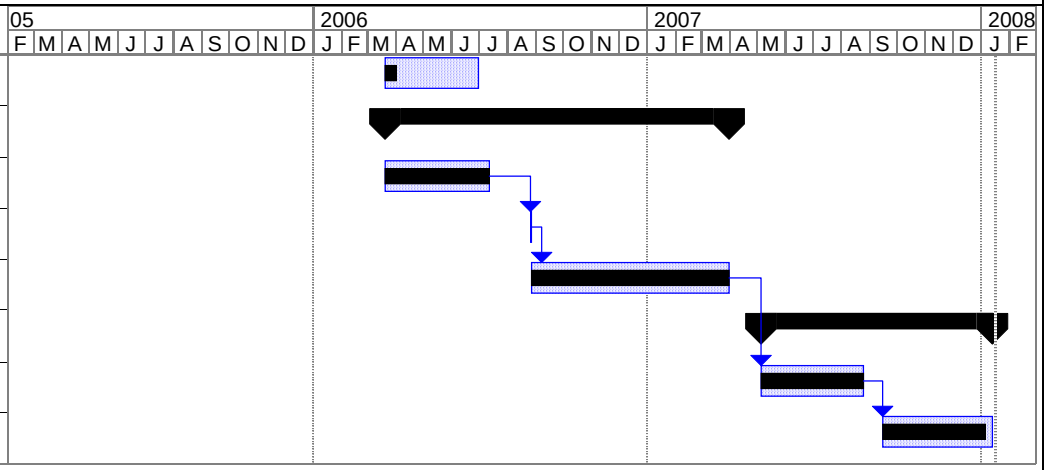

Budget Amount $ 2,400,000

Paid to Date: $ 0

Task | Milestone
Progress | Summary

Project Description: Park renovation.

Current Status: Commission approval in Jan 07. Construction 98% complete (1/18).
